Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	15 February 2025
Team ID	
Project Name	Team Enrollment Confirmation - Import Data using Transform Maps (Spreadsheet)
Team Size	4
Team Leader	SRIKAVI T
Team Members	ISWARYA S, YOGASRI S, KEERTHIKA L
Maximum Marks	5 Marks

1. Product Backlog, Sprint Schedule, and Estimation (4 Marks)

The product backlog below breaks the Team Enrollment Confirmation project into four sprints of 20 story points each (80 story points in total). The project uses a spreadsheet as the data source and Transform Maps to import the data into the Team Enrollment table.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Data Source Setup	USN-1	As a team leader, I can prepare the enrollment spreadsheet (Excel) with team member name, email, role and enrollment status columns.	3	High	Srikavi T
Sprint-1	Data Source Setup	USN-2	As an admin, I can create the Team Enrollment custom table with all required fields to store the imported data.	5	High	Iswarya S
Sprint-1	Data Source Setup	USN-3	As an admin, I can configure user roles and access controls (ACL) for the Team Enrollment table.	3	Medium	Yogasri S
Sprint-1	Data Source Setup	USN-4	As an admin, I can load the spreadsheet as a data source and create the Import Set table.	5	High	Keerthika L
Sprint-1	Data Source Setup	USN-5	As a team member, I can validate the file format, column headers and sample data before import.	4	High	Srikavi T
Sprint-2	Transform Map Configuration	USN-6	As an admin, I can create a Transform Map from the Import Set table to the Team Enrollment table.	5	High	Iswarya S

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-2	Transform Map Configuration	USN-7	As an admin, I can map source fields to target fields so each spreadsheet column lands in the correct field.	4	High	Yogasri S
Sprint-2	Transform Map Configuration	USN-8	As an admin, I can coalesce on the email field so duplicate enrollment records are not created.	3	High	Keerthika L
Sprint-2	Transform Map Configuration	USN-9	As an admin, I can add a transform script to clean data (trim spaces, standardize case) during import.	4	Medium	Srikavi T
Sprint-2	Transform Map Configuration	USN-10	As an admin, I can run the transform and verify that records are imported into the target table.	4	High	Iswarya S
Sprint-3	Enrollment Confirmation	USN-11	As an admin, I can add an Enrollment Status field with choices Pending, Confirmed and Rejected.	3	High	Yogasri S
Sprint-3	Enrollment Confirmation	USN-12	As an admin, I can create a business rule that sets status to Confirmed when all required details are present.	5	High	Keerthika L
Sprint-3	Enrollment Confirmation	USN-13	As a team member, I will receive a confirmation email once my enrollment is confirmed.	5	High	Srikavi T
Sprint-3	Enrollment Confirmation	USN-14	As a team leader, I can view a list and report of confirmed enrollments.	4	Medium	Iswarya S
Sprint-3	Enrollment Confirmation	USN-15	As an admin, I can review import logs and skipped or ignored rows to correct errors.	3	Medium	Yogasri S
Sprint-4	Testing & Deployment	USN-16	As a tester, I can import a valid dataset and confirm all records are transformed correctly.	4	High	Keerthika L
Sprint-4	Testing & Deployment	USN-17	As a tester, I can import invalid and duplicate data and confirm it is handled properly.	4	High	Yogasri S
Sprint-4	Testing & Deployment	USN-18	As a team, we can perform user acceptance testing and fix reported defects.	5	High	Iswarya S
Sprint-4	Testing & Deployment	USN-19	As a team leader, I can prepare the project documentation and final demo.	4	Medium	Srikavi T
Sprint-4	Testing & Deployment	USN-20	As an admin, I can move the completed configuration to the final instance using an update set.	3	Medium	Keerthika L

2. Project Tracker, Velocity & Burndown Chart (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	20	6 Days	24 Oct 2022	29 Oct 2022	20	29 Oct 2022
Sprint-2	20	6 Days	31 Oct 2022	05 Nov 2022		
Sprint-3	20	6 Days	07 Nov 2022	12 Nov 2022		
Sprint-4	20	6 Days	14 Nov 2022	19 Nov 2022		

Velocity


Each sprint has a duration of 6 days and a total of 20 story points, so the team's velocity is 20 story points per sprint.

Average velocity (AV) per day = Velocity / Sprint duration = 20 / 6 = 3.33 story points per day

Across the whole project: 80 story points over 4 sprints (24 days) gives the same 3.33 story points per day. For the 10-day example in the template (20 points per sprint), AV = 20 / 10 = 2 story points per day.

Burndown Chart

A burndown chart is a graphical representation of work left to do versus time. It is often used in agile software development methodologies such as Scrum, but it can be applied to any project with measurable progress over time.

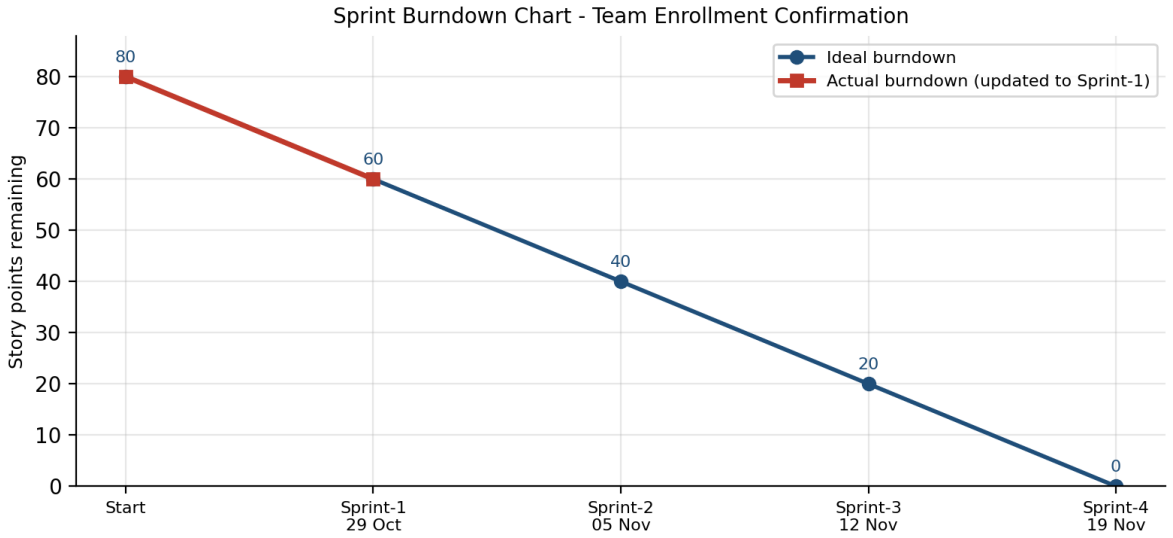

Sprint End	Planned Points Burned	Ideal Points Remaining	Actual Points Remaining
Start	-	80	80
Sprint-1 (29 Oct 2022)	20	60	60
Sprint-2 (05 Nov 2022)	20	40	
Sprint-3 (12 Nov 2022)	20	20	
Sprint-4 (19 Nov 2022)	20	0	

Actual values for Sprint-2 to Sprint-4 are to be filled in as each sprint completes.

Reference

https://www.atlassian.com/agile/project-management
https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software
https://www.atlassian.com/agile/tutorials/epics
https://www.atlassian.com/agile/tutorials/sprints
https://www.atlassian.com/agile/project-management/estimation
https://www.atlassian.com/agile/tutorials/burndown-charts
https://www.visual-paradigm.com/scrum/scrum-burndown-chart/
